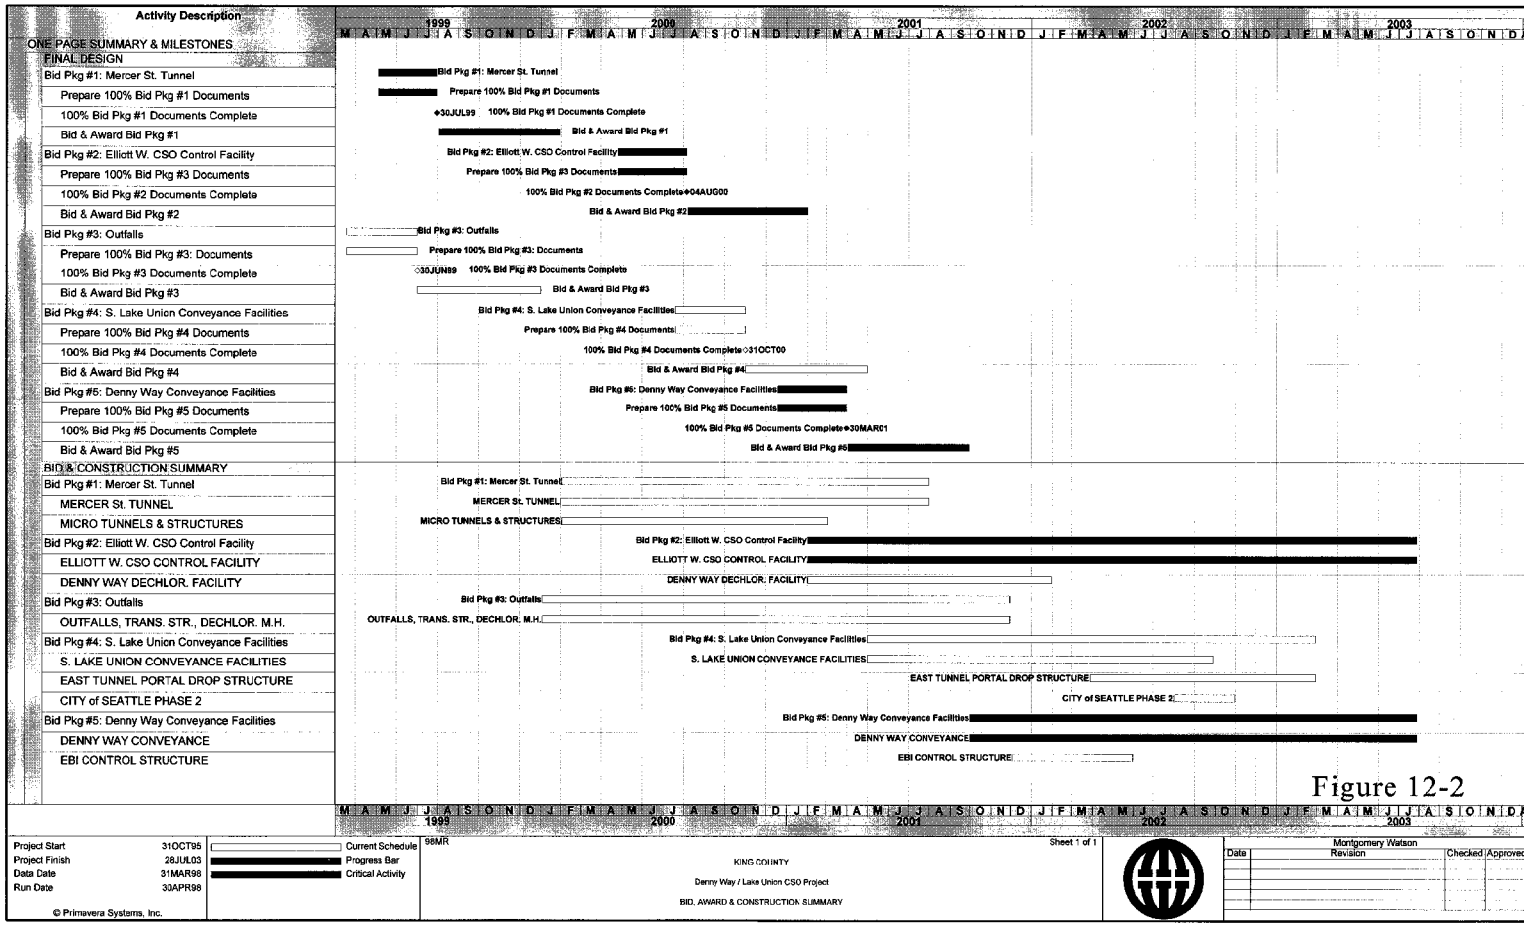
Activity Description
1999
2000
2001
2002
2003
ONE PAGE SUMMARY & MILESTONES
FINAL DESIGN
Bid Pkg #1: Mercer St. Tunnel
Prepare 100% Bid Pkg #1 Documents
100% Bid Pkg #1 Documents Complete
Bid & Award Bid Pkg #1
Bid Pkg #2: Elliott W. CSO Control Facility
Prepare 100% Bid Pkg #3 Documents
100% Bid Pkg #2 Documents Complete
Bid & Award Bid Pkg #2
Bid Pkg #3: Outfalls
Prepare 100% Bid Pkg #3: Documents
100% Bid Pkg #3 Documents Complete
Bid & Award Bid Pkg #3
Bid Pkg #4: S. Lake Union Conveyance Facilities
Prepare 100% Bid Pkg #4 Documents
100% Bid Pkg #4 Documents Complete
Bid & Award Bid Pkg #4
Bid Pkg #5: Denny Way Conveyance Facilities
Prepare 100% Bid Pkg #5 Documents
100% Bid Pkg #5 Documents Complete
Bid & Award Bid Pkg #5
BID & CONSTRUCTION SUMMARY
Bid Pkg #1: Mercer St. Tunnel
MERCER St. TUNNEL
MICRO TUNNELS & STRUCTURES
Bid Pkg #2: Elliott W. CSO Control Facility
ELLIOTT W. CSO CONTROL FACILITY
DENNY WAY DECHLOR. FACILITY
Bid Pkg #3: Outfalls
OUTFALLS, TRANS. STR., DECHLOR. M.H.
Bid Pkg #4: S. Lake Union Conveyance Facilities
S. LAKE UNION CONVEYANCE FACILITIES
EAST TUNNEL PORTAL DROP STRUCTURE
CITY of SEATTLE PHASE 2
Bid Pkg #5: Denny Way Conveyance Facilities
DENNY WAY CONVEYANCE
EBI CONTROL STRUCTURE
30JUL99
30JUN99
04AUG00
31OCT00
30MAR01
Project Start 31OCT95
Project Finish 28JUL03
Data Date 31MAR98
Run Date 30APR98
Current Schedule
Progress Bar
Critical Activity
© Primavera Systems, Inc.
98MR
Sheet 1 of 1
KING COUNTY
Denny Way / Lake Union CSO Project
BID, AWARD & CONSTRUCTION SUMMARY
Montgomery Watson
Date
Revision
Checked
Approved

Figure 12-2
