KING COUNTY - NORTH CREEK STORAGE FACILITY

FIGURE 3

ID	Task Name	Duration	Start	Finish	Predecessors
1	**North Creek Storage Facility**	**786 days**	**Thu 12/30/99**	**Thu 1/2/03**	
2	Finalize Contract/ Scope of Work	20 days	Thu 12/30/99	Wed 1/26/00	
3	**Final Design**	**209 days**	**Thu 12/30/99**	**Tue 10/17/00**	
4	Finalize Storage Volume	20 days	Thu 12/30/99	Wed 1/26/00	
5	Finalize Design Parameters	25 days	Thu 1/27/00	Wed 3/1/00	2
6	Geotechnical Investigation	15 days	Thu 1/27/00	Wed 2/16/00	2
7	Geotechnical Report	20 days	Thu 2/17/00	Wed 3/15/00	6
8	Mechanical Design	35 days	Thu 3/2/00	Wed 4/19/00	5
9	Site Civil Design	35 days	Thu 3/2/00	Wed 4/19/00	5
10	Structural Design	35 days	Thu 3/16/00	Wed 5/3/00	7
11	Electrical Design	20 days	Thu 3/30/00	Wed 4/26/00	8SS+20 days
12	HVAC Design	20 days	Thu 3/30/00	Wed 4/26/00	8SS+20 days
13	50% Design Documents	0 days	Wed 5/3/00	Wed 5/3/00	8,9,10,11,12
14	VE Review of Design	20 days	Thu 5/4/00	Wed 5/31/00	13
15	Address VE Comments	15 days	Thu 6/1/00	Wed 6/21/00	14
16	Prepare 100% Design	40 days	Thu 6/22/00	Wed 8/16/00	15
17	100% Design Documents	0 days	Wed 8/16/00	Wed 8/16/00	16
18	Review of 100% Design	20 days	Thu 8/17/00	Wed 9/13/00	17
19	Incorporate Comments into Bid Documents	20 days	Thu 9/14/00	Wed 10/11/00	18
20	Print Documents	4 days	Thu 10/12/00	Tue 10/17/00	19
21	**Project Permits**	**131 days**	**Wed 3/1/00**	**Thu 8/31/00**	
22	SEPA Checklist	60 edays	Wed 3/1/00	Sun 4/30/00	5
23	City of Bothell Grading Permit	120 edays	Wed 5/3/00	Thu 8/31/00	13,22
24	City of Bothell Building Permit	120 edays	Wed 5/3/00	Thu 8/31/00	13,22
25	City of Bothell Right-of-Way Invasion Permit	120 edays	Wed 5/3/00	Thu 8/31/00	13,22
26	City of Bothell Construction Review	120 edays	Wed 5/3/00	Thu 8/31/00	13,22
27	PSAPCA Notice of Construction	90 edays	Wed 5/3/00	Tue 8/1/00	13
28	**Construction**	**577 days**	**Tue 10/17/00**	**Thu 1/2/03**	
29	Advertise for Bid	30 edays	Tue 10/17/00	Thu 11/16/00	20,26
30	Open and Evaluate Bids	5 days	Fri 11/17/00	Thu 11/23/00	29
31	Award of Contract	0 days	Thu 11/23/00	Thu 11/23/00	30
32	Notice to Proceed for Construction	0 days	Thu 12/21/00	Thu 12/21/00	31FS+20 days
33	Construct Storage Facility	700 edays	Thu 12/21/00	Thu 11/21/02	32
34	Acceptance Testing	30 days	Fri 11/22/02	Thu 1/2/03	33
35	Facility On-Line	0 days	Thu 1/2/03	Thu 1/2/03	34

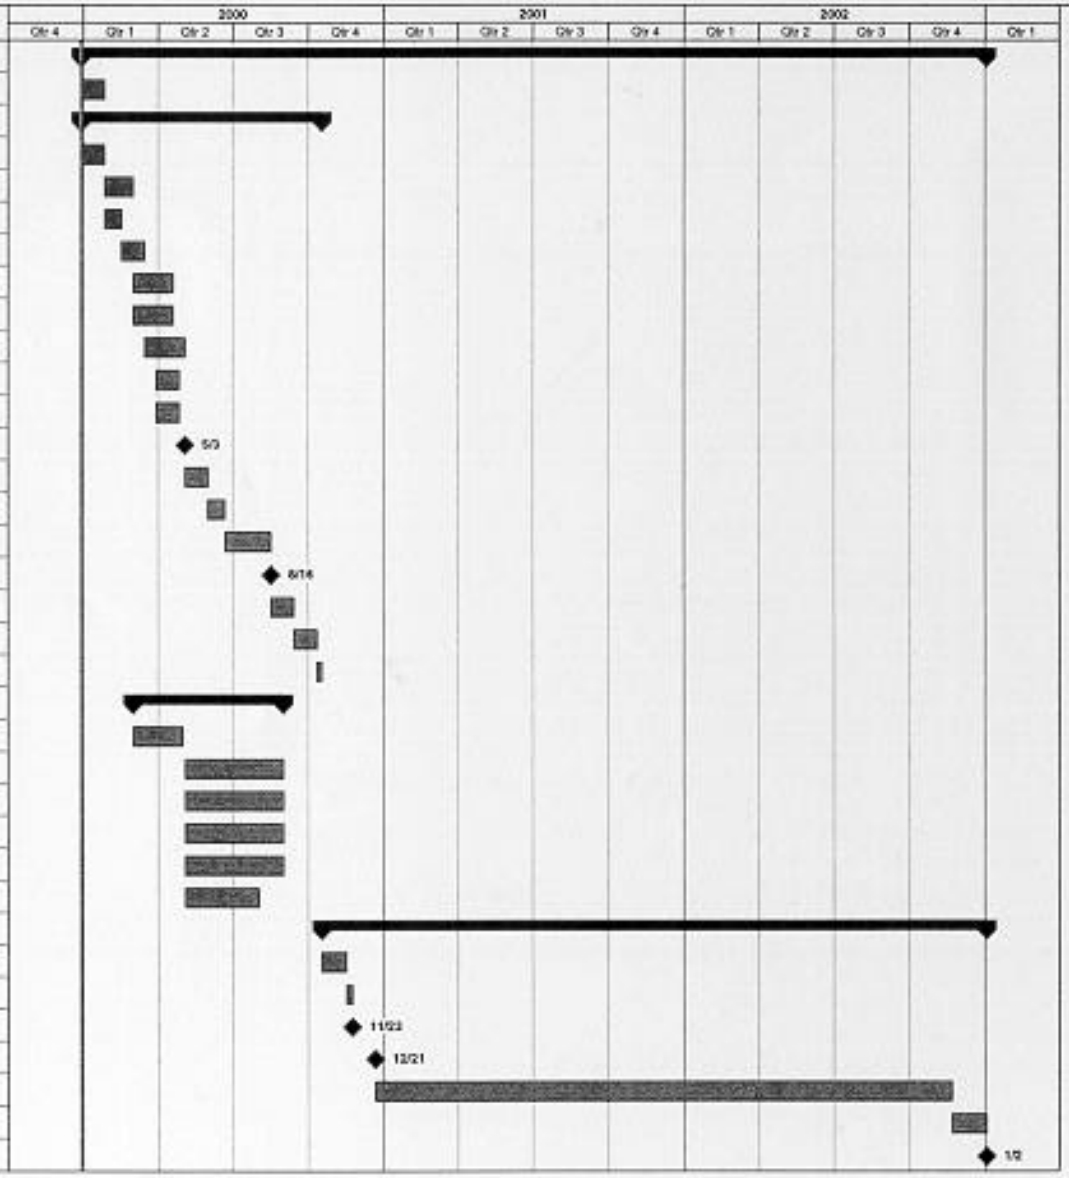

Task | Progress | Milestone | Summary | Project Summary | Split

HDR ENGINEERING, INC
